

**Inspection report of 15 MLD STP Unnao of 1200 mm dia RCC pipe laying,Cleaning,desilting & jointing dated 28.02.25**



70 nos pipe laying completed and step cutting work is in progress




Feb 28, 2025 14:28:15  
Unnamed Road  
Charlestown Institutional Area  
Unnao  
Lucknow Division  
Uttar Pradesh



Feb 28, 2025 11:08:29  
Supasi  
Lucknow Division  
Uttar Pradesh

Borewell no 74 is in progress & 2<sup>nd</sup> lift concrete work completed of MH no 42



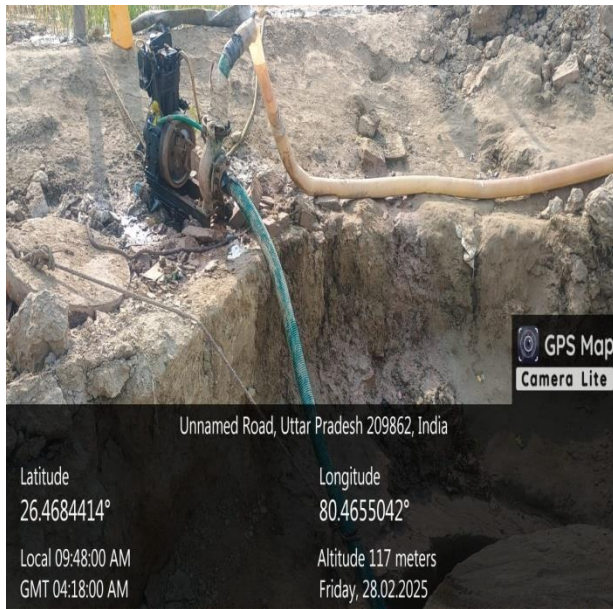

Dewatering and desilting work at MH 36-37 & Desilting work at MH 38



Desilting work at MH-14 & Jointing work

**1200 MM DIA RCC SEWER LINE AT 15 MLD STP UNNAO**

**28.02.2025**

SL. No.	Pipe Dia.(mm)	Manhole No.		Total Sewer line Length	Desilting Done	Re-Cleaning Done	New Pipe line Laying Done	Remark
		From	To					
1	1200	IND	1	13.10	Completed	Completed	-	WIP
2	1200	1	2	92.70	Completed	Completed	-	
3	1200	2	4	69.30	Completed	Completed	-	Jointing WIP
4	1200	4	5	101.10	Completed	Completed	-	
5	1200	5	6	45.30	Completed	Completed	-	
6	1200	6	11	125.00	Completed	Completed	-	
7	1200	11	12	42.44	Completed	Completed	-	
8	1200	12	13	90.84	Completed	WIP	-	
9	1200	13	14	18.55	Completed	WIP	-	WIP
10	1200	14	15	99.60	Completed	WIP	-	
11	1200	15	16	130.80	Completed	Pending	-	
12	1200	16	17	38.20	Completed	Pending	-	
13	1200	17	19	50.39	Completed		-	
14	1200	19	110	93.45	Completed	Completed	-	
15	1200	110	21A	82.57	Completed	Completed	-	
16	1200	21A	21	22.50	Completed	Pending	-	
17	1200	21	22	105.00	Completed	Pending	-	
18	1200	22	111	32.50	Completed	Pending	-	
19	1200	111	23	32.50	Completed	Pending	-	
20	1200	23	112	40.00	Completed	Pending	-	
21	1200	112	24	52.50	Completed	Pending	-	
22	1200	24	25	75.00	Completed	Pending	-	
23	1200	25	113	72.50	Completed	Pending	-	
24	1200	113	26	45.00	Completed	Pending	-	
25	1200	26	27	97.50	Completed	Pending	-	
26	1200	27	28	92.50	Completed	Pending	-	
27	1200	28	29	75.00	Completed	Pending	-	
28	1200	29	30	107.50	Completed	Pending	-	
29	1200	30	31	80.00	Completed	Pending	-	
30	1200	31	116	72.50	Not Completed	-	-	
31	1200	116	33	75.00	Completed	Pending	-	
32	1200	33	34	105.00	Completed	Pending	-	
33	1200	34	35A	25.00	Completed	Pending	-	
34	1200	35A	35	55.00	Completed	Completed	-	
35	1200	35	36	95.00	Completed	Completed	-	
36	1200	36	37	110.00	Not Completed	WIP	-	
37	1200	37	38	90.00	Not Completed		-	
38	1200	38	39A	120.95	Not Completed		-	
NEW LINE								
39	1200	39A	40	96.50	Laying Pending	-	-	
40	1200	40	41	82.00	Laying Pending	-	WIP	
41	1200	41	42	45.00	Completed	-	Completed	
42	1200	42	43	91.80	Completed	-	Completed	
43	1200	43	44	60.00	Laying Pending	-	-	
44	1200	44	REC	24.50	Laying Pending	-	-	
Total				3171.56				

**1200 MM DIA RCC SEWER LINE PROGRES REPORT AT 15 MLD STP UNNAO (1569)**

					Date	28.02.2025
Work Description Summary	Scope (Mtr.)	Work Done (Previous)	Work Done (Today)	Work done (Cummalitive)	Balance Work (As on date)	Manpower Status
Desilting Line	543.45	227.00	2.00	229.00	314.45	18
Re-Checking	2,228.31	723.00	20.00	743.00	1,485.31	13
New Pipe line Laying	399.80	182.50	-	182.50	217.30	28
Summary:-	3,171.56	1,132.50	22.00	1,154.50	2,017.06	59.00
