

Salient point of 15 MLD STP Unnao dated 30.09.24

Followings are highlights

1. It was advised that by 1/10/24. 2 nos of pump should be checked which are installed in MPS .So many times it has been written but no attention has been paid.
 - Tomorrow Hydra should reach without fail for dismantling of pumps.
 - Although EOT is installed but lift height problem is there.
 - It was advised to make channel and install it to use EOT lifting in installment.



2. Balance of plant PLC connection work was in progress.
3. Manpower should be deployed without if and but by 03/09/24 for fabrication of suitable size cable trench covers from Checker plates which were available at site.
4. Expedite the OEM team for commissioning of chlorination plant. Commissioning is long pending.
5. One mechanical screen was non operational. Please get it checked.




6. Both organic pump was non operational. Similarly both Screw conveyors to be attended.
7. Commissioning of DG set is pending which needs walk way all around foundation which has not been made since long.
8. Flow meters are to be calibrated properly. Discharge readings of inflow are less than outflow.
9. In one centrifuge decanter there is Censor problem. Please attend.
10. Earthing, Road Outside lighting poles installation, Site development, Wall making, painting etc all are pending.



11. No work of Laying new 1200 mm RCC pipes have started nor cleaning and checking of layed pipes. Work has started. Still water level is high, 350 m 1200 dia RCC pipe was at site.



12. During the inspection it was found that chlorine dosing was not being done.

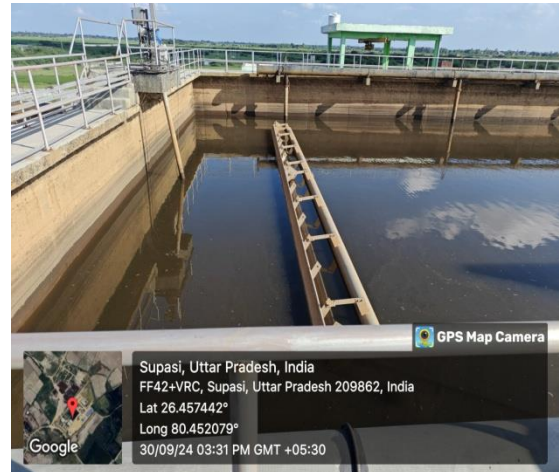

13. Centrifuge machine was not running.

