

Jajmau 130 MLD STP Inspection report dated 20/06/2025



Lube oil installarion, Raditor side HT & LT pipe line welding & Panel work in progress



PLC cable dressing & gland fitting near main PLC room



OnePlus 12R

24mm 171.8 1/1674s 15064



OnePlus 12R


24mm 171.8 1/1378s 15064

Ventilation & gas dome installation work in progress



OnePlus 12R

24mm 171.8 1/71s 15064

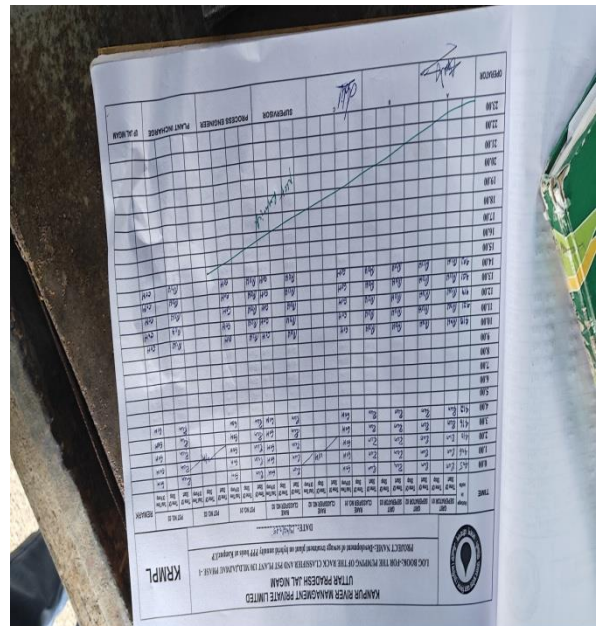

OnePlus 12R

24mm 171.8 1/50s 150250

PTU & Mechanical screen & log book register



OnePlus 12R

24mm 01.8 1/1280x ISO50



OnePlus 12R

24mm 01.8 1/1450x ISO50

PST & Aeration Tank



OnePlus 12R

24mm 01.8 1/1450x ISO50



OnePlus 12R

24mm 01.8 1/500x ISO50

BFP 2 operational out of 4, chlorination non operational



OnePlus 12R

24mm 1/1.8 1/107s ISO50



OnePlus 12R

24mm 1/1.8 1/475s ISO50

TEPH Pump & labour without safety kit



OnePlus 12R

24mm 1/1.8 1/3753s ISO64

Pump repair work & metering room

- KRMPL to submit the work plan for all balance works.
- All three wings of KRMPL (Civil, Mechanical & Electrical) must coordinate to speed up progress.
- Work clearances should be provided mutually between departments without delay.
- Some individual unit works should be taken up in parallel.
- Advance planning is essential to complete works on time.
- Any shortfall in materials should be identified, expedited, and arranged promptly.
- Power failure was observed during the recent site visit – requires immediate resolution.
- Shade on the PTU is broken and needs replacement.
- Safety concerns were noted – action is required to improve safety conditions.
- Chlorination process is not being carried out – needs to be started immediately.
- Both screens in CSPS are non-operational – require repair or replacement.
- Air tightness testing for Primary Digesters 1 & 2 is pending.
- Cleaning work of the Secondary Digester is yet to be completed.
- Painting work is pending for all structures, including:
 - All panel rooms
 - TSPH
 - DSPH
 - RSPH
 - Admin building
- The following works are also pending:
 - Door and window installation
 - Glass and earthing work
 - Exhaust fan installation
 - Drainage system setup
 - Site development
 - Plastering and finishing of the ventilation room
